Owner: Government of the District of Columbia
Department of Transportation
Project Name: Civil Infrastructure Construction for the District of Columbia Power Line Undergrounding
(DC PLUG) Feeder 15166
Contract No.: DCKA-2023-C-0019

Submitted by:

Capitol Paving of D.C., Inc.
2211 Channing St. NE
Washington, D.C. 20018
202.529.7225

3 WEEK LOOK AHEAD CONSTRUCTION SCHEDULE

Period From: 6-Jan-25 to: 25-Jan-25 | Data Date: 30-Dec-24

Activity ID	Description	Location	Resource	Planned Start	Planned Finish	Actual % as of DD
PEPCO Material Fabrication and Procurement				4-Mar-24		
PROC-1000	Order, Procure & Pick Up of PEPCO Supplied Materials (Lebaum St. SE)		CPDC	4-Mar-24	25-Jan-25	
PROC-1010	Order, Procure & Pick Up of PEPCO Supplied Materials (Martin Luther King Jr. Ave. SE)		CPDC	4-Mar-24	25-Jan-25	
PROC-1020	Order, Procure & Pick Up of PEPCO Supplied Materials (Mellon St. SE)		CPDC	4-Mar-24	25-Jan-25	
PROC-1060	Order, Procure & Pick Up of PEPCO Supplied Materials (Malcolm X Ave. SE)		CPDC	4-Mar-24	25-Jan-25	
Project Requirements				29-May-24		
REQ-1000	Duct Inspection and Certification (Lebaum St. SE)	500 Block Lebaum St. SE	CPDC-UTL3	4-Dec-24	18-Dec-24	100%
REQ-1010	Duct Inspection and Certification (Martin Luther King Jr. Ave. SE)	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL3	4-Dec-24	19-Dec-24	100%
REQ-1020	Duct Inspection and Certification (Mellon St. SE)	400-500 Blocks Mellon St. SE	CPDC-UTL3	4-Dec-24	24-Dec-24	100%
REQ-1060	Duct Inspection and Certification (Malcolm X Ave. SE)	Unit-500 Blocks Malcolm X Ave. SE	CPDC-UTL3	4-Dec-24	27-Dec-24	100%
Construction Phase				4-Mar-24		
2nd St. SE/Newcomb St. SE				18-Mar-24		
Oakwood St. SE/4th St/5th St/Orange St. SE				4-Apr-24		
Oakwood-1105	~~Install SSB#8~~ Install a 4.5'x6x7' CIP Manhole PENDING FOR CHANGE ORDER APPROVAL	Orange St SE (72' East of 2nd St SE	Anchor-UTL2	20-Jan-25	25-Jan-25	
Oakwood-1290	Sawcutting on Various Locations	Various Locationswithin the project limits	CPDC Saw	26-Aug-24	21-Dec-24	
Malcolm X Ave. SE				13-May-24		
Malcolm-1220	PCC Pavement Restoration Malcolm X Ave. SE-Newcomb St to Martin Luther King Jr. Ave. SE	500 Block Malcolm X Ave. SE	CPDC-UTL1	9-Dec-24	20-Dec-24	100%
Malcolm-1280	Mill and Overlay Malcolm X Ave. SE-Oakwood St to Martin Luther King Jr. Ave. SE	500 Block Malcolm X Ave. SE	CPDC Asphalt	18-Dec-24	30-Dec-24	100%
Malcolm-1300	Pavement Markings and Signage Malcolm X Ave. SE	500 Block Malcolm X Ave. SE	CPDC Line	26-Dec-24	3-Jan-25	
Martin Luther King Jr. Ave. SE				13-May-24		
MLK-1070	PCC Pavement Restoration Martin Luther King Jr. Ave SE-Lebaum St to Mellon St.	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL1	3-Dec-24	20-Dec-24	
MLK-1080	PCC Pavement Restoration Martin Luther King Jr. Ave SE- Mellon St. to Malcolm X Ave. PENDING FOR CHANGE ORDER APPROVAL	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL1	5-Dec-24		
MLK-1100	Mill and Overlay Martin Luther King Jr. Ave SE-Mellon St. to Malcolm X Ave.	2900 Block Martin Luther King Jr. Ave. SE	CPDC Asphalt	18-Dec-24	27-Dec-24	
MLK-1110	Pavement Markings and Signage Martin Luther King Jr. Ave SE	2900 Block Martin Luther King Jr. Ave. SE	CPDC Line	26-Dec-24	3-Jan-25	
Lebaum St. SE				10-Jun-24		
Lebaum-1150	Pavement Markings and Signage Lebaum St. SE	500 Block Lebaum St. SE	CPDC Line	26-Dec-24	3-Jan-25	
Mellon St. SE				7-Jun-24		
	Install conduits on TE#13, Fix TH#5 and install conduits	423 Mellon St. SE, Newcomb St and Malcolm X Ave. SE	CPDC-UTL1	17-Dec-24	18-Dec-24	100%
	Fix obstruction b/w MH8 and MH#36	Newcomb St and Malcolm X Ave. SE	CPDC-UTL1	19-Dec-24	24-Dec-24	100%
	Clean Manholes, Install Grounding Rod	Various locations	CPDC-UTL2	23-Dec-24	27-Dec-24	
Mellon-1070	Install ~~SSB#2~~ Install a 4.5'x6x7' CIP Manhole PENDING FOR CHANGE ORDER APPROVAL	465Mellon St. SE	Anchor-UTL1	20-Jan-25	25-Jan-25	
Mellon-1070	Install ~~SSB#3~~ Install a 4.5'x6x7' CIP Manhole PENDING FOR CHANGE ORDER APPROVAL	511 Mellon St. SE	Anchor-UTL1	27-Jan-25	1-Feb-25	
Mellon-1070	Install P~~SB#4~~ Install a 4.5'x6x7' CIP Manhole PENDING FOR CHANGE ORDER APPROVAL	525 Mellon St. SE	Anchor-UTL2	27-Jan-25	1-Feb-25	

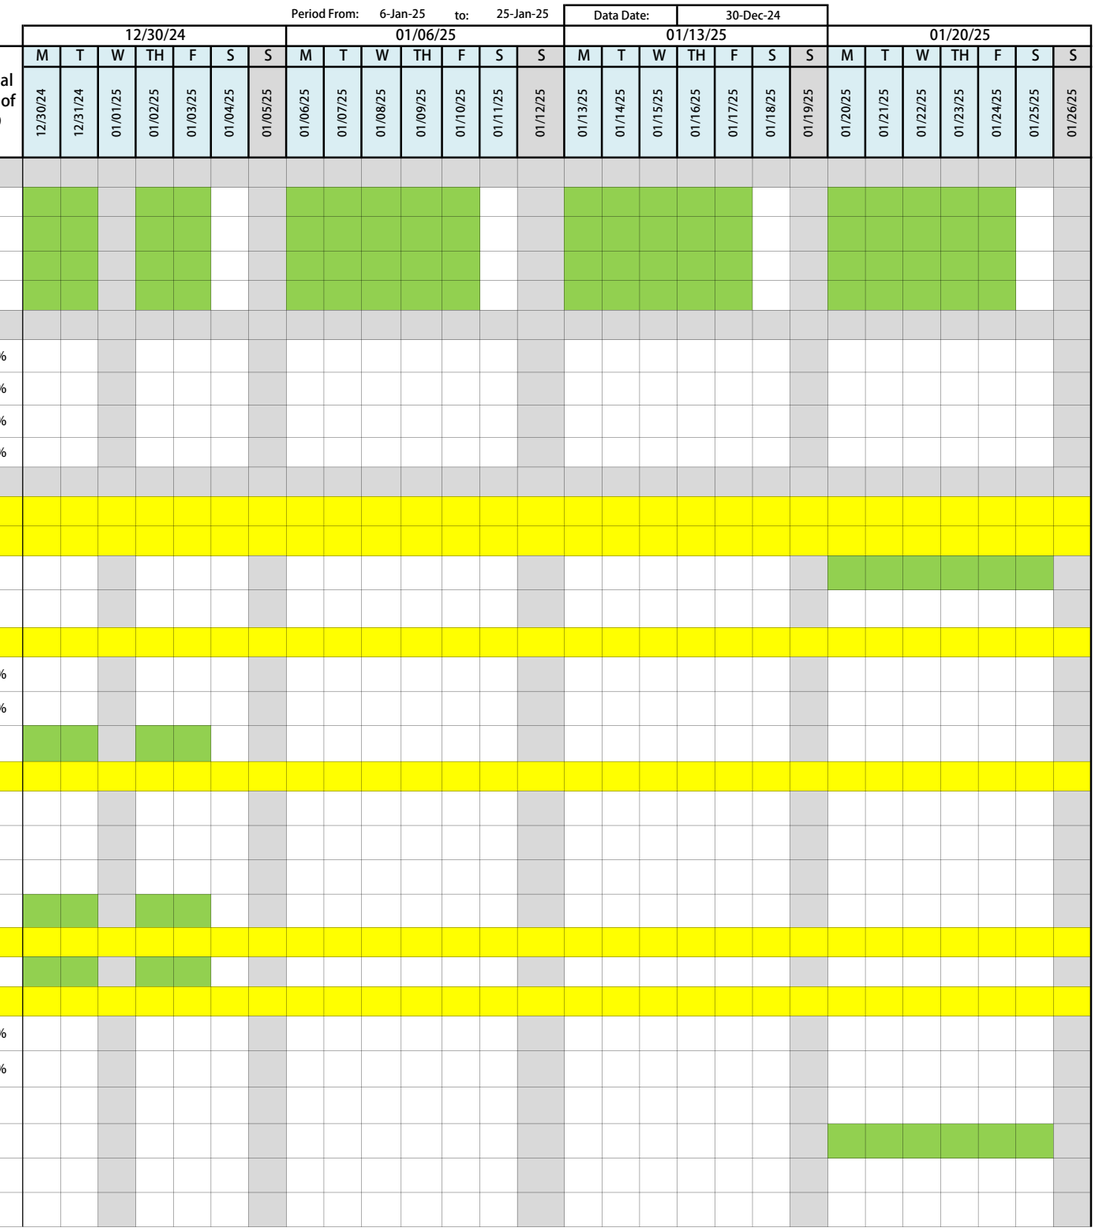

MA
