Owner: Government of the District of Columbia
Department of Transportation
Project Name: Civil Infrastructure Construction for the District of Columbia Power Line Undergrounding
(DC PLUG) Feeder 15166
Contract No.: DCKA-2023-C-0019

Submitted by:

Capitol Paving of D.C., Inc.
2211 Channing St. NE
Washington, D.C. 20018
202.529.7225

3 WEEK LOOK AHEAD CONSTRUCTION SCHEDULE

Period From: 4-Nov-24 to: 23-Nov-24 | Data Date: 28-Oct-24

Activity ID	Description	Location	Resource	Planned Start	Planned Finish	Actual % as of DD
PEPCO Material Fabrication and Procurement				4-Mar-24		
PROC-1000	Order, Procure & Pick Up of PEPCO Supplied Materials (Lebaum St. SE)		CPDC	4-Mar-24	30-Nov-24	
PROC-1010	Order, Procure & Pick Up of PEPCO Supplied Materials (Martin Luther King Jr. Ave. SE)		CPDC	4-Mar-24	30-Nov-24	
PROC-1020	Order, Procure & Pick Up of PEPCO Supplied Materials (Mellon St. SE)		CPDC	4-Mar-24	30-Nov-24	
PROC-1060	Order, Procure & Pick Up of PEPCO Supplied Materials (Malcolm X Ave. SE)		CPDC	4-Mar-24	30-Nov-24	
Project Requirements				29-May-24		
REQ-1000	Duct Inspection and Certification (Lebaum St. SE)	500 Block Lebaum St. SE	CPDC-UTL3	20-Nov-24	22-Nov-24	
REQ-1010	Duct Inspection and Certification (Martin Luther King Jr. Ave. SE)	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL3	20-Nov-24	22-Nov-24	
REQ-1020	Duct Inspection and Certification (Mellon St. SE)	400-500 Blocks Mellon St. SE	CPDC-UTL3	28-Oct-24	28-Oct-24	
Construction Phase				4-Mar-24		
Oakwood St. SE/4th St/5th St/Orange St. SE				4-Apr-24		
Oakwood-1290	Sawcutting on Various Locations	Various Locationswithin the project limits	CPDC Saw	26-Aug-24	16-Nov-24	
Malcolm X Ave. SE				13-May-24		
Malcolm-1150	Install Conduits MH#8 to MH#9	500 Block Malcolm X Ave. SE	CPDC-UTL2	18-Nov-24	23-Nov-24	
Malcolm-1160	Install Manhole Recess on Malcolm X Ave. SE-Newcomb St. SE to Martin Luther King Jr. Ave. SE	500 Block Malcolm X Ave. SE	CPDC-UTL2	28-Oct-24	4-Nov-24	
Martin Luther King Jr. Ave. SE				13-May-24		
MLK-1030	Install Conduits SMH#1 to MH#12	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL1	4-Nov-24	5-Nov-24	
MLK-1040	Install Conduits MH#12 to MH#18	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL1	5-Nov-24	6-Nov-24	
MLK-1050	Install Conduits MH#18 to SMH#3	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL1	6-Nov-24	8-Nov-24	
MLK-1060	Install Conduits SMH#3 to MH#11	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL2	18-Nov-24	23-Nov-24	
MLK-1060	Install Manhole Recess onMartin Luther King Jr. Ave SE-Lebaum St to Mellon St.	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL2	11-Nov-24	16-Nov-24	
MLK-1070	PCC Pavement Restoration Martin Luther King Jr. Ave SE-Lebaum St to Mellon St.	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL1	18-Nov-24	20-Nov-24	
MLK-1080	PCC Pavement Restoration Martin Luther King Jr. Ave SE-Mellon St to Mellon St. Malcolm X Ave.	2900 Block Martin Luther King Jr. Ave. SE	CPDC-UTL1	20-Nov-24	23-Nov-24	
Lebaum St. SE				10-Jun-24		
Lebaum-1095	Install Conduits MH#16 to MH#17	500 Block Lebaum St. SE	CPDC-UTL1	30-Oct-24	31-Oct-24	
Lebaum-1100	Install Conduits MH#17 to SMH#1	500 Block Lebaum St. SE	CPDC-UTL1	31-Oct-24	4-Nov-24	
Lebaum-1100	Install Manhole Recess on Lebaum St. SE	400-500 Blocks Lebaum St. SE	CPDC-UTL2	5-Nov-24	9-Nov-24	
	Install IMH#1 on Lebaum St. SE (Pending for Change Order Approval)	500 Block Lebaum St. SE	CPDC-UTL2	5-Nov-24	6-Nov-24	
Lebaum-1110	Asphalt Base/PCC Pavement Restoration Lebaum St. SE-Martin Luther King Jr. Ave to 5th St. SE	500 Block Lebaum St. SE	CPDC-UTL1	11-Nov-24	15-Nov-24	

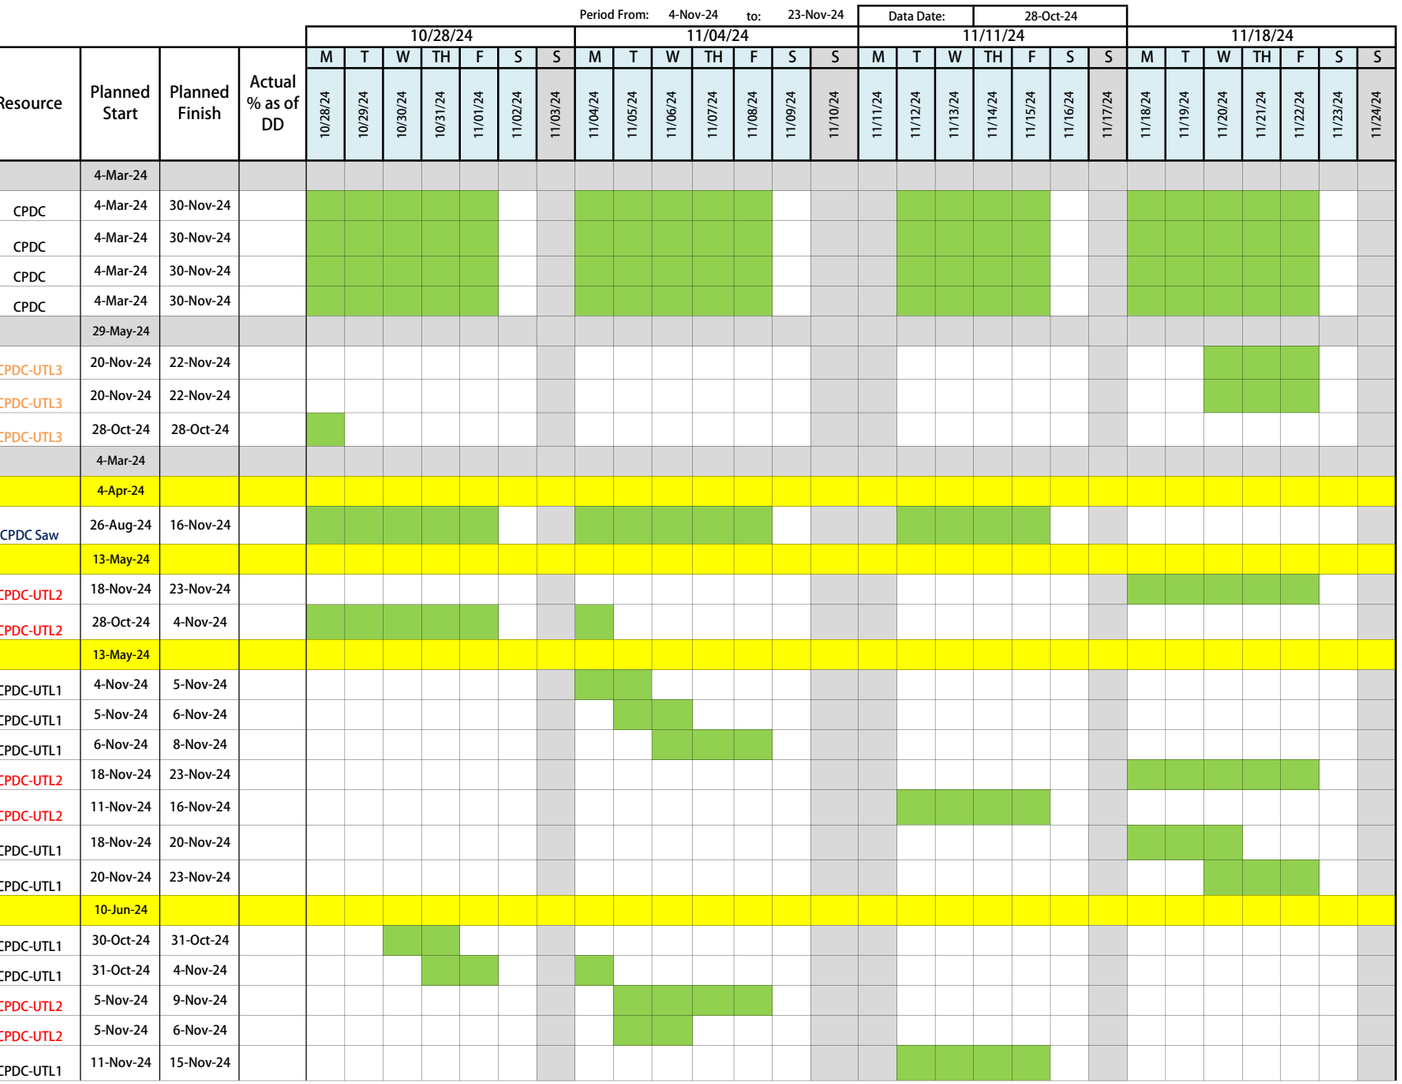

MA

Owner: Government of the District of Columbia
Department of Transportation
Project Name: Civil Infrastructure Construction for the District of Columbia Power Line Undergrounding
(DC PLUG) Feeder 15166
Contract No.: DCKA-2023-C-0019

Submitted by:

Capitol Paving of D.C., Inc.
2211 Channing St. NE
Washington, D.C. 20018
202.529.7225

3 WEEK LOOK AHEAD CONSTRUCTION SCHEDULE

Period From: 4-Nov-24 to: 23-Nov-24 | Data Date: 28-Oct-24

Activity ID	Description	Location	Resource	Planned Start	Planned Finish	Actual % as of DD	10/28/24							11/04/24							11/11/24							11/18/24						
							M	T	W	TH	F	S	S	M	T	W	TH	F	S	S	M	T	W	TH	F	S	S	M	T	W	TH	F	S	S
							10/28/24	10/29/24	10/30/24	10/31/24	11/01/24	11/02/24	11/03/24	11/04/24	11/05/24	11/06/24	11/07/24	11/08/24	11/09/24	11/10/24	11/11/24	11/12/24	11/13/24	11/14/24	11/15/24	11/16/24	11/17/24	11/18/24	11/19/24	11/20/24	11/21/24	11/22/24	11/23/24	11/24/24
Mellon St. SE				7-Jun-24																															
Mellon-1150	Asphalt Base/PCC Pavement Restoration Mellon St. SEand 5th St. to Martin Luther King Jr. Ave. SE	500 Block Mellon St. SE	CPDC-UTL1	23-Oct-24	29-Oct-24																														
Mellon-1160	Mill and Overlay Mellon St. SE-4th St. to 5th St. SE	400 Block Mellon St. SE	CPDC Asphalt	30-Oct-24	1-Nov-24																														
Mellon-1170	Mill and Overlay Mellon St. SEand 5th St. to Martin Luther King Jr. Ave. SE	500 Block Mellon St. SE	CPDC Asphalt	30-Oct-24	1-Nov-24																														
Mellon-1180	Pavement Markings and Signage Mellon St. SE, 5th St. SE	400-500 Blocks Mellon St. SE	CPDC Line	1-Nov-24	4-Nov-24																														

MA
