LOOK AHEAD SCHEDULE

PROJECT: DC PLUG FEEDER 15001 Civil Construction

CAPITOL PAVING OF D.C., INC

Week Start: Mon, 8/26/2024
Today Date: Wed, 8/28/2024
Display Week: 1

ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
DCKA-2023-C-042_BL.3	**Submittals and Shop Drawings**				**4/3/2024**		**147**
DCKA-2023-C-042_BL.5.1	**DUCT INSPECTION**						
INS1000	Duct Insp & Cert - PH1	CPDC	Blagden Ter b/w 17th and Colorado Ave	60%	9/4/24	9/6/24	2.00
INS1000	Duct Insp & Cert - PH1	CPDC	Colorado Ave NW b/w 16th and 17th St	60%	9/4/24	9/6/24	2.00
DCKA-2023-C-042_BL.6	**Pre-Construction**				**4/15/2024**		**135**
FAB1010	Order & Procure PEPCO Precast Structures & Conduit 50%	CPDC		80%	5/16/24	9/18/24	126.00
PRE1030	Project Stake Out & Lay Out	CPDC		50%	4/3/24	5/3/24	31.00
PRE1040	Mark Exiting Utilities	CPDC	Phase 2	60%	5/20/24	5/31/24	12.00
	Taking In Situ Soil Sample	CPDC	13th St, Colorado Ave, Madison St, Jefferson St	100%	8/13/24	8/14/24	2.00
DCKA-2023-C-042_BL.7.3	**Phase 1.0**				**4/29/2024**		**121**
UG Utility					**4/29/2024**		**121**
	Install TEs, THs, 4.5x6 MHs	Miguel E	14th St NW b/w Emerson & Gallatin St	90%	8/22/24	8/23/24	2.00
PH4-UT-1470	Install TMH3	CPDC-UTL1	5521 Colorado Ave NW	50%	8/27/24	8/30/24	4.00
PH4-UT-1460	Install TMH6	CPDC-UTL1	5617 Colorado Ave NW	50%	8/27/24	8/30/24	4.00
PH2-UT-1350	Install MH66b	CPDC-UTL1	5201 16th St NW, Washington, DC	0%	9/2/24	9/6/24	5.00
PH2-UT-1340	Install SMH6	CPDC-UTL1	5201 16th St NW, Washington, DC	0%	9/2/24	9/6/24	5.00
PH4-UT-1440	Install 6x12 MH7	CPDC-UTL1	5617 Colorado Ave NW	0%	9/9/24	9/13/24	5.00
PH3-UT-1220	Install MH87	CPDC-UTL1	5623 Colorado Ave NW	0%	9/9/24	9/13/24	5.00
PH4-UT-1430	Install TMH8	CPDC-UTL1	5617 Colorado Ave NW	0%	9/9/24	9/13/24	5.00
PH4-UT-1410	Install 6x12 MH9	CPDC-UTL1	1314 Madison st NW	0%	9/16/24	9/20/24	5.00
PH4-UT-1400	Install SMH2	CPDC-UTL1	1301 Madison St NW	0%	9/16/24	9/20/24	5.00
PH4-UT-1390	Install 6x12 MH10	CPDC-UTL1	1214 Madison St NW	0%	9/23/24	9/27/24	5.00
PH4-UT-1380	Install SMH3	CPDC-UTL1	1214 Madison St NW	0%	9/23/24	9/27/24	5.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Longefellow St b/w Colorado ave to 13th	0%	8/30/24	8/31/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Ingraham St b/w 14th to Colorado Ave	0%	9/5/24	9/6/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Hamilton St b/w 14th to PB	0%	9/5/24	9/6/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Gallatin St b/w 14th to PB	0%	9/5/24	9/6/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	13th St b/w Madison to Kennedy	0%	9/12/24	9/13/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	13th St b/w Madison to Kennedy	0%	9/19/24	9/20/24	2.00
	Install MH Sump Pit and Grounding PH1	Miguel E		90%	6/17/24	7/5/24	19.00
UG CONDUIT					**4/29/2024**		**121**
PH1-UT-1110	Install Conduit - Blagden Ave b/w Allison & Mathews	CPDC-UTL2		70%	8/14/24	9/6/24	23.00
PH2-UT-1530	Install Conduit - Decatur b/w 16th St to 18th	CPDC-UTL2		0%	9/6/24	9/20/24	14.00
PH1-UT-1110	Backfill - Blagden Ave b/w Allison & Mathews	CPDC-UTL2		70%	8/14/24	9/6/24	23.00
PH2-UT-1530	Backfill - Decatur b/w 16th to 18th	CPDC-UTL2		0%	9/6/24	9/20/24	14.00
	MH Recess - Blagden Ave b/w Allison & Mathews	CPDC-UTL3		70%	8/14/24	9/6/24	23.00
	MH Recess - Decatur b/w 16th to 18th	CPDC-UTL3		0%	9/6/24	9/20/24	14.00
PCC PVMT					**5/24/2024**		**96**
PH1-PVMT-1020	PCC Restoration - Blagden Ave b/w 18th & 17th	CPDC-Armando		0%	8/26/24	8/30/24	4.00
PH1-PVMT-1010	PCC Restoration - Blagden Ave b/w Allison & 18th St	CPDC-Armando		0%	9/2/24	9/6/24	4.00
PH1-PVMT-1000	PCC Restoration - Blagden Ave b/w Allison & Matthew	CPDC-Armando		0%	9/9/24	9/20/24	11.00
ASPHALT PVMT					**6/10/24**		**79**

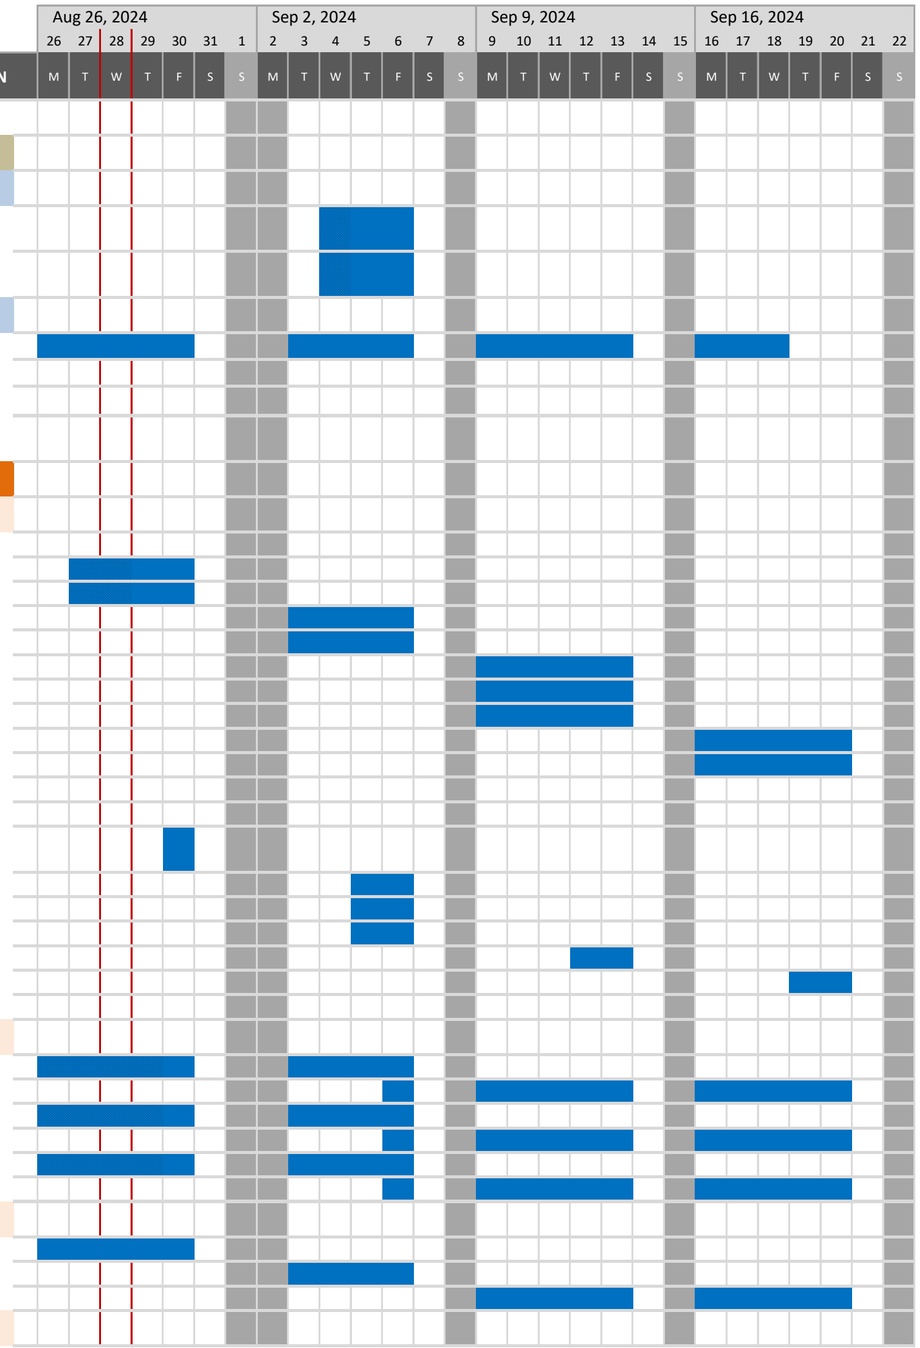

EST. 1987

Display Week: 1

ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
PH1-ASPH-1010	Mill & Pave Colorado Ave b/w 16th St and 17th St			85%	8/26/24	8/30/24	4.00
PH1-ASPH-1000	Mill & Pave Blagden Ave b/w 16th St		16th to 18th St	0%	9/4/24	9/12/24	8.00
PVMT MARKINGS					**6/10/2024**		**79**



Note: Activities are tentative on weather conditions or other unforseen conditions
Saturday work may be requested on weekly basis to Engineer for review and approval
