Owner: Government of the District of Columbia
Department of Transportation
Project Name: Civil Infrastructure Construction for the District of Columbia Power Line Undergrounding
DC PLUG Feeder 118 / 14702
Contract No.: DCKA-2024-C-0073

Submitted by:

Capitol Paving of D.C., Inc.
2211 Channing St. NE
Washington, D.C. 20018
202.529.7225

3 WEEK LOOK AHEAD CONSTRUCTION SCHEDULE

Period From: 10-Mar-25 to: 30-Mar-25 | Data Date: 10-Mar-25

Activity ID	Description	Location	Resource	Planned Start	Planned Finish	Actual % as of DD
Project Submittals and Requirements				7-Mar-25		
PSUBM-1000	Prepare and Submit DDOT Materials Submittals		CPDC	7-Mar-25	14-Mar-25	
PSUBM-1010	Engineers Review and Approval of DDOT Materials Submittals		CPDC	7-Mar-25	28-Mar-25	
PEPCO Material Fabrication and Procurement				11-Mar-25		
PROC-1000	Order, Procure & Pick Up of PEPCO Supplied Materials (Ridge Pl. SE and 22nd St. SE from Q St to S St. SE)		CPDC	11-Mar-25	30-Apr-25	
PROC-1010	Order, Procure & Pick Up of PEPCO Supplied Materials (25th St., Palmer Pl., Q St., and 26th St. SE)		CPDC	11-Mar-25	30-Apr-25	
PROC-1020	Order, Procure & Pick Up of PEPCO Supplied Materials (28th St., 28th Pl., 29th St., Q St., R St., S St., Texas Ave. SE)		CPDC	11-Mar-25	30-Apr-25	
PROC-1030	Order, Procure & Pick Up of PEPCO Supplied Materials (N St., O St., 28th St., 29th St., 30th St., Nash Pl. SE)		CPDC	11-Mar-25	30-Apr-25	
Pre-Construction Phase				7-Mar-25		
PRE-1010	Prepare Engineers Field Facilities		CPDC	7-Mar-25	7-Mar-25	100%
PRE-1020	Pre-Construction Survey		CPDC	11-Mar-25	21-Mar-25	
PRE-1030	Field Lay Out, Preconstruction Photos and Videos		CPDC	10-Mar-25	21-Mar-25	
PRE-1040	Marking of Existing Utilities (Missutility)		CPDC	7-Mar-25	21-Mar-25	
Construction Phase				11-Mar-25		
CONS-1000	Project Mobilization		CPDC	11-Mar-25	11-Mar-25	100%
CONS-1010	Install Erosion and Sediment Control Devices		CPDC	11-Mar-25	21-Mar-25	
CONS-1020	Install DC PLUG Signs, Portable Message and Traffic Control Signs, Set-up Staging Area		CPDC	11-Mar-25	21-Mar-25	
CONS-1030	Performed Test Pits & Soil Samples		CPDC	11-Mar-25	21-Mar-25	
Ridge Pl. SE and 22nd St. SE from Q St to S St. SE				24-Mar-25		
22nd St-1010	Install MH#6	1700 Block 22nd St. SE	CPDC-UTL1	24-Mar-25	25-Mar-25	
22nd St-1010	Install MH#7, MH#8, MH#9	1600-1700 Blocks 22nd St. SE	CPDC-UTL1	27-Mar-25	28-Mar-25	
22nd St-1020	Install TH#3,TH#4,	1600-1700 Blocks 22nd St. SE	CPDC-UTL1	25-Mar-25	26-Mar-25	
22nd St-1020	Install TE#5	1700 Block 22nd St. SE	CPDC-UTL1	26-Mar-25	26-Mar-25	
22nd St-1020	Install TE#6	1600 Block 22nd St. SE	CPDC-UTL1	28-Mar-25	28-Mar-25	
Ridge-1000	Install MH#1, MH#2	1900-2000 Blocks Ridge Pl. SE	CPDC-UTL1	24-Mar-25	25-Mar-25	
Ridge-1000	Install MH#3, MH#4	2200-2300 Blocks Ridge Pl. SE	CPDC-UTL1	27-Mar-25	28-Mar-25	
Ridge-1010	Install TE#1, TE#2, TH#1	1900-2000 Blocks Ridge Pl. SE	CPDC-UTL1	25-Mar-25	26-Mar-25	
Ridge-1020	Install TH#2, TE#3, TE#4	2200 Block Ridge Pl. SE	CPDC-UTL1	25-Mar-25	26-Mar-25	
25th St., Palmer Pl., Q St., and 26th St. SE				31-Mar-25		
25th St-1000	Install MH#15, MH#16, MH#17	1400-1600 Blocks 25th St. SE	CPDC-UTL1	3-Apr-25	4-Apr-25	
26th Pl.-1000	Install MH#13, MH#14, TE#10	1600 Block 26th Pl. SE	CPDC-UTL1	2-Apr-25	3-Apr-25	
Q St.-1000	Install MH#10, MH#11, MH#12	2300-2500 Blocks Q St. SE	CPDC-UTL2	1-Apr-25	2-Apr-25	
Q St.-1010	Install TE#7, TE#8, TH#5, TE#9, TH#6	2300-2500 Blocks Q St. SE	CPDC-UTL2	31-Mar-25	1-Apr-25	
28th St., 28th Pl., 29th St., Q St., R St., S St., Texas Ave. SE				13-Mar-25		
28th St.-1150	Install MH#44 (6'x12')	1600 Block 28th St. SE	CPDC-UTL1	14-Apr-25	18-Apr-25	
28th St.-1160	Install TMH#8 (6'x14')	1700 Block 28th St. SE	CPDC-UTL1	14-Apr-25	18-Apr-25	
28th St.-1170	Install MH#51 (6'x12'), MH#50 (6'x12')	1700 Block 28th St. SE	CPDC-UTL1	7-Apr-25	11-Apr-25	

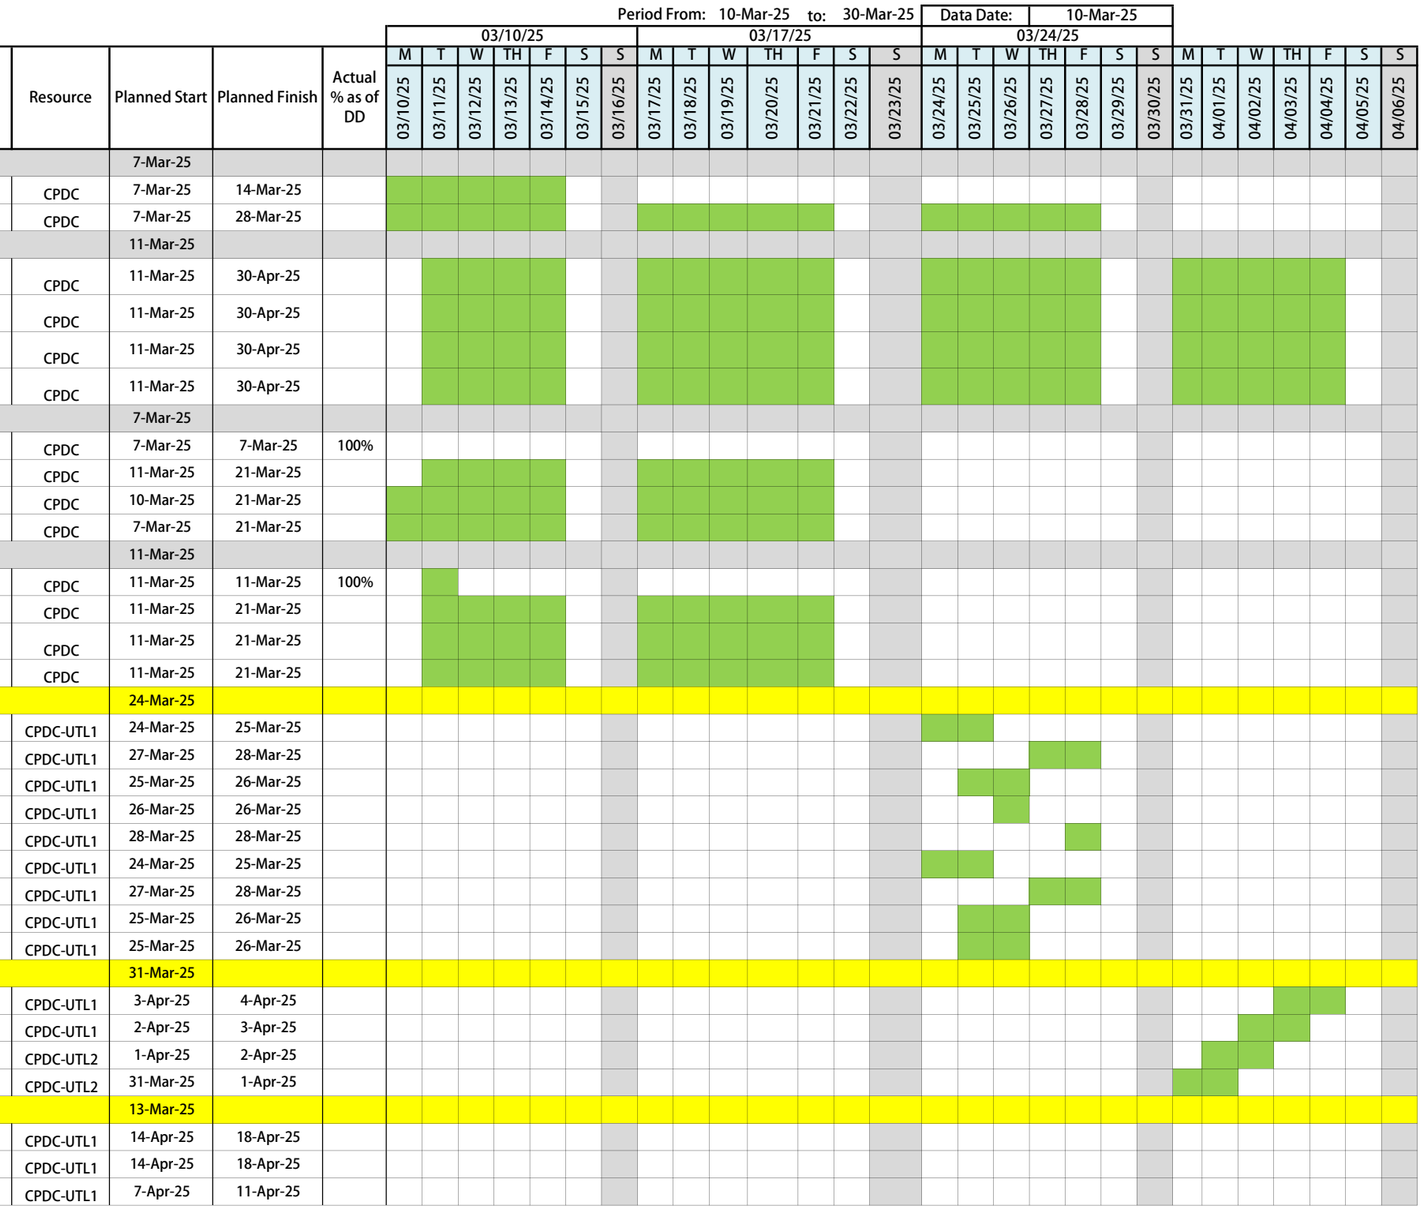

Notes: Saturday works will be requested to DDOT for approval

MA
